


#	Name	Duration	2012											
			Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
1	<b>Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen</b>	185 days	[Summary bar spanning Jan to Sep]											
2	Start Date for this Plan	0 days	[Milestone diamond]											
3	<b>A - ASSEMBLE SDT</b>	6 days	[Green bar in Jan]											
4	SC Appoints DT	5 days	[Green bar in Jan]											
5	Hold Pre-project Meeting with DT Leaders	1 days	[Green bar in Jan]											
6	Assembly Complete	0 days	[Milestone diamond]											
7	<b>B - DRAFT STANDARD</b>	22 days	[Green bar in Jan]											
8	Write Draft Standard	10 days	[Green bar in Jan]											
9	Send Posting Package to SPM for Quality Review	2 days	[Green bar in Jan]											
10	Perform Quality Review of Posting Package	5 days	[Green bar in Jan]											
11	Edit Posting Package based on QR and Send to SPM	2 days	[Green bar in Jan]											
12	Final Pre-Posting Review of Posting Package	2 days	[Green bar in Jan]											
13	Drafting Complete	0 days	[Milestone diamond]											
14	<b>E - INITIAL BALLOT</b>	39 days	[Green bar in Feb]											
15	Write Draft Standard Posting and Ballot Pool Announcement	2 days	[Green bar in Feb]											
16	Post Draft Standard and Update Web Page	2 days	[Green bar in Feb]											
17	Post Draft Standard Posting and Ballot Pool Announcement	2 days	[Green bar in Feb]											
18	Distribute Draft Standard Posting and Ballot Pool Announcement	2 days	[Green bar in Feb]											
19	VAR-002 Rapid Revision Comment Period REF_POST_FBI	45 edays	[Green bar in Feb]											

Project: Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen  
Planned Start: 3/23/11      Projected Start: 1/11/12  
Planned Completion: 10/1/12      Projected Completion: 10/1/12  
Printed On: 7/18/12

Asks for clarification of whether a GOP must communicate to a TOP that a generator is in manual mode (no AVR) during start up or shut down.

Planned		Projected	
Overdue		In Progress	
Summary		Complete	
Milestone		Predecessor	



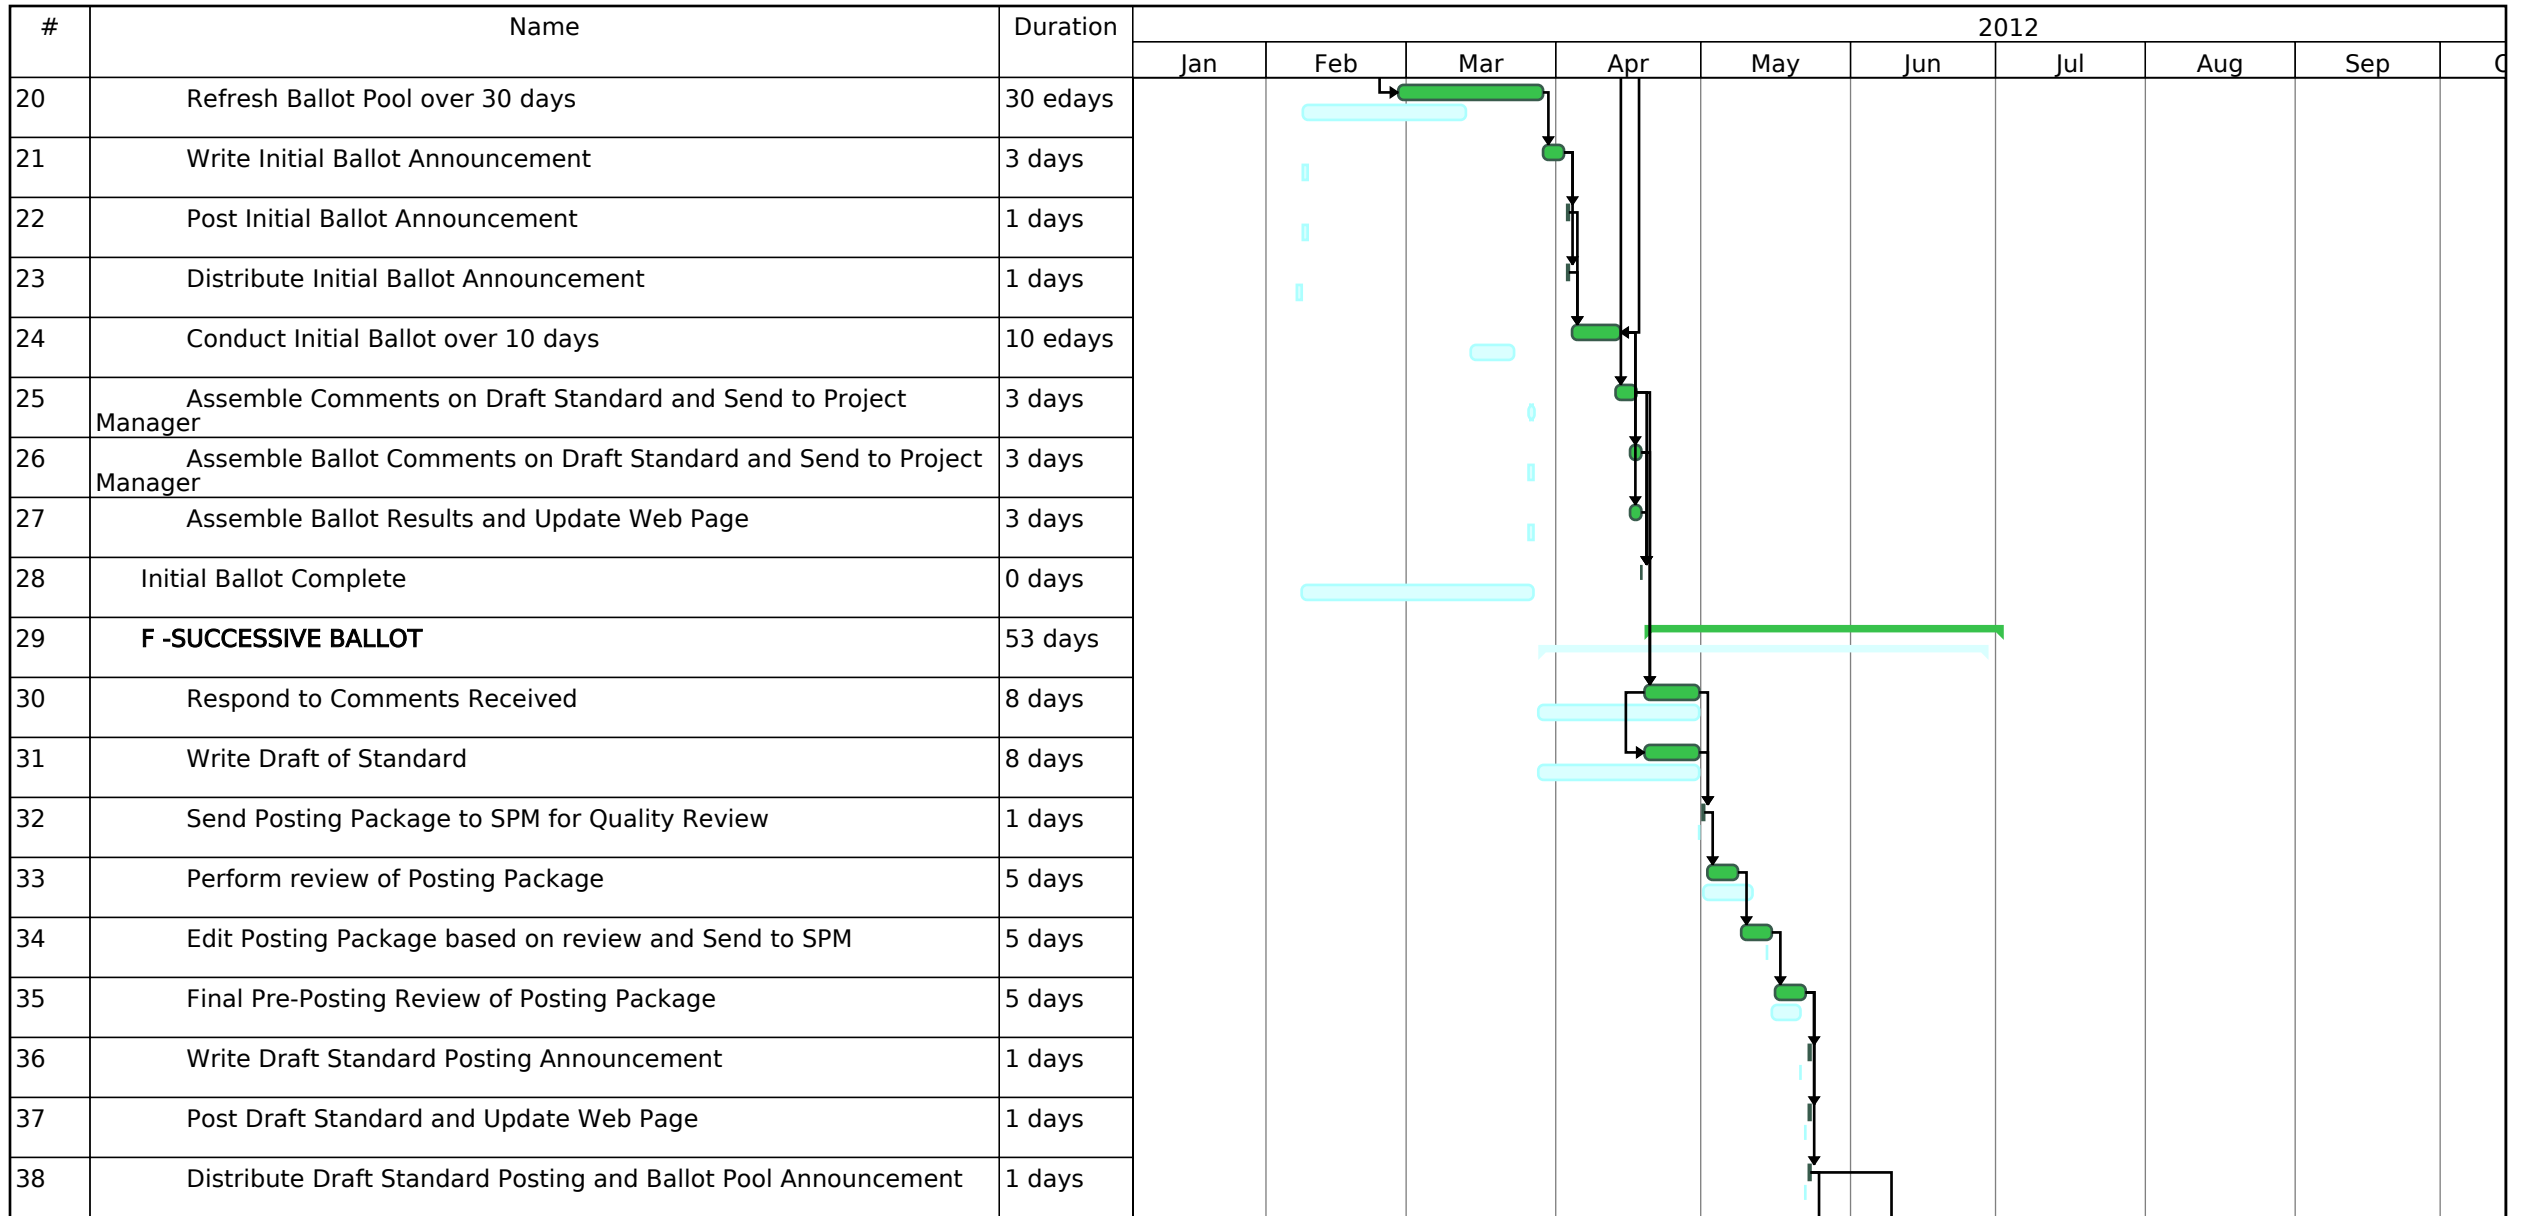

Project: Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen  
 Planned Start: 3/23/11      Projected Start: 1/11/12  
 Planned Completion: 10/1/12      Projected Completion: 10/1/12  
 Printed On: 7/18/12


Asks for clarification of whether a GOP must communicate to a TOP that a generator is in manual mode (no AVR) during start up or shut down.







#	Name	Duration	2012														
			Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct					
77	Send Draft Filing to Standard Regulatory Initiatives	1 days															
78	Perform Standards Regulatory Initiatives Review	5 days															
79	Edit Draft Filing based on SRI Review and send to Legal	3 days															
80	Perform Legal Review	5 days															
81	Edit Draft Filing based on Legal Review and send to Exec Mgmt	3 days															
82	Perform Exec Mgmt Review	5 days															
83	Edit Draft Filing based on Exec Mgmt Review	3 days															
84	Assemble development record	5 days															
85	Assemble Final Filing Package	1 days															
86	Submit Final Filing Package	1 days															
87	Filing Complete	0 days															



Project: Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen  
 Planned Start: 3/23/11      Projected Start: 1/11/12  
 Planned Completion: 10/1/12      Projected Completion: 10/1/12  
 Printed On: 7/18/12

Page 5


Asks for clarification of whether a GOP must communicate to a TOP that a generator is in manual mode (no AVR) during start up or shut down.

Planned		Projected	
Overdue		In Progress	
Summary		Complete	
Milestone		Predecessor	

			2013														
Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	M

Project: Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen  
 Planned Start: 3/23/11      Projected Start: 1/11/12  
 Planned Completion: 10/1/12      Projected Completion: 10/1/12  
 Printed On: 7/18/12

Asks for clarification of whether a GOP must communicate to a TOP that a generator is in manual mode (no AVR) during start up or shut down.








Planned		Projected	
Overdue		In Progress	
Summary		Complete	
Milestone		Predecessor	



			2013														
Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	M

Project: Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen  
 Planned Start: 3/23/11      Projected Start: 1/11/12  
 Planned Completion: 10/1/12      Projected Completion: 10/1/12  
 Printed On: 7/18/12


Asks for clarification of whether a GOP must communicate to a TOP that a generator is in manual mode (no AVR) during start up or shut down.

Planned		Projected	
Overdue		In Progress	
Summary		Complete	
Milestone		Predecessor	

			2013														
Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	M

Project: Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen  
 Planned Start: 3/23/11      Projected Start: 1/11/12  
 Planned Completion: 10/1/12      Projected Completion: 10/1/12  
 Printed On: 7/18/12

Asks for clarification of whether a GOP must communicate to a TOP that a generator is in manual mode (no AVR) during start up or shut down.

Planned		Projected	
Overdue		In Progress	
Summary		Complete	
Milestone		Predecessor	





			2013														
Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	M

Project: Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen  
 Planned Start: 3/23/11      Projected Start: 1/11/12  
 Planned Completion: 10/1/12      Projected Completion: 10/1/12  
 Printed On: 7/18/12

Asks for clarification of whether a GOP must communicate to a TOP that a generator is in manual mode (no AVR) during start up or shut down.




Planned		Projected	
Overdue		In Progress	
Summary		Complete	
Milestone		Predecessor	

			2013														
Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	M

Project: Project 2011-INT-02 Interpretation of VAR-002 for Constellation Power Gen  
 Planned Start: 3/23/11      Projected Start: 1/11/12  
 Planned Completion: 10/1/12      Projected Completion: 10/1/12  
 Printed On: 7/18/12

Page 10

Asks for clarification of whether a GOP must communicate to a TOP that a generator is in manual mode (no AVR) during start up or shut down.

Planned		Projected	
Overdue		In Progress	
Summary		Complete	
Milestone		Predecessor	

